

1. Work requester fills out this section.

☐ Standing Work Permit

Requester: Don Lynch	Date: 10/21/2008	Ext.: 2253	Dept/Div/Group: PO/PHENIX
Other Contact person (if different from requester): Carter Biggs			Ext.: 7515
Work Control Coordinator: Don Lynch		Start Date: 10/20/2008	Est. End Date: 2/1/09
Brief Description of Work: Install RPC2 Prototype			
Building: 1008	Room: IR	Equipment: RPC	Service Provider: PHENIX techs & RPC experts

WCC, Requester/Designee, Service Provider, and ES&H (as necessary) fill out this section or attach analysis

<b>ES&amp;H ANALYSIS</b>					
<b>Radiation Concerns</b>		<input checked="" type="checkbox"/> None	<input type="checkbox"/> Activation	<input type="checkbox"/> Airborne	<input type="checkbox"/> Contamination
Radiation Generating Devices:		<input type="checkbox"/> Radiography	<input type="checkbox"/> Moisture Density Gauges	<input type="checkbox"/> Soil Density Gauges	<input type="checkbox"/> X-ray Equipment
<input type="checkbox"/> Special nuclear materials involved, notify Isotope Special Materials Group			<input type="checkbox"/> Fissionable materials involved, notify Laboratory Criticality Officer		
<b>Safety Concerns</b>		<input checked="" type="checkbox"/> None	<input type="checkbox"/> Ergonomics	<input type="checkbox"/> Transport of Haz/Rad Material	
<input type="checkbox"/> Adding/Removing Walls or Roofs	<input checked="" type="checkbox"/> Confined Space*	<input type="checkbox"/> Explosives	<input type="checkbox"/> Lead*	<input type="checkbox"/> Penetrating Fire Walls	
	<input type="checkbox"/> Corrosive	<input type="checkbox"/> Flammable	<input type="checkbox"/> Magnetic Field*	<input type="checkbox"/> Pressurized Systems	
<input type="checkbox"/> Asbestos*	<input type="checkbox"/> Cryogenic	<input type="checkbox"/> Fumes/Mist/Dust*	<input type="checkbox"/> Material Handling	<input type="checkbox"/> Rigging/Critical Lift	
<input type="checkbox"/> Beryllium*	<input type="checkbox"/> Electrical	<input type="checkbox"/> Heat/Cold Stress	<input type="checkbox"/> Noise*	<input type="checkbox"/> Toxic Materials*	
<input type="checkbox"/> Biohazard*	<input checked="" type="checkbox"/> Elevated Work*	<input type="checkbox"/> Hydraulic	<input type="checkbox"/> Non-ionizing Radiation*	<input type="checkbox"/> Vacuum	
<input type="checkbox"/> Chemicals*	<input type="checkbox"/> Excavation	<input type="checkbox"/> Lasers*	<input type="checkbox"/> Oxygen Deficiency*	<input type="checkbox"/> Other	
* Does this work require medical clearance or surveillance from the Occupational Medicine Clinic? <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No					
<b>Environmental Concerns</b>		<input checked="" type="checkbox"/> None	<input type="checkbox"/> Work impacts Environmental Permit No.		
<input type="checkbox"/> Atmospheric Discharges (rad/non-rad)	<input type="checkbox"/> Land Use	<input type="checkbox"/> Soil Activation/contamination	<input type="checkbox"/> Waste-Mixed		
<input type="checkbox"/> Chemical or Rad Material Storage or Use	<input type="checkbox"/> Liquid Discharges	<input type="checkbox"/> Waste-Clean	<input type="checkbox"/> Waste-Radioactive		
<input type="checkbox"/> Cesspools (UIC)	<input type="checkbox"/> Oil/PCB Management	<input type="checkbox"/> Waste-Hazardous	<input type="checkbox"/> Waste-Regulated Medical		
<input type="checkbox"/> High water/power consumption	<input type="checkbox"/> Spill potential	<input type="checkbox"/> Waste-Industrial	<input type="checkbox"/> Underground Duct/Piping		
Waste disposition by:		<input type="checkbox"/> Other			
<b>Pollution Prevention (P2)/Waste Minimization Opportunity:</b>		<input checked="" type="checkbox"/> None <input type="checkbox"/> Yes			
<b>FACILITY CONCERNS</b>		<input checked="" type="checkbox"/> None			
<input type="checkbox"/> Access/Egress Limitations	<input type="checkbox"/> Electrical Noise	<input type="checkbox"/> Potential to Cause a False Alarm		<input type="checkbox"/> Vibrations	
	<input type="checkbox"/> Impacts Facility Use Agreement		<input type="checkbox"/> Temperature Change		<input type="checkbox"/> Other
<input type="checkbox"/> Configuration Control	<input type="checkbox"/> Maintenance Work on Ventilation Systems		<input type="checkbox"/> Utility Interruptions		
<b>WORK CONTROLS</b>					
<b>Work Practices</b>					
<input checked="" type="checkbox"/> None	<input type="checkbox"/> Exhaust Ventilation	<input checked="" type="checkbox"/> Lockout/Tagout	<input type="checkbox"/> Spill Containment	<input type="checkbox"/> Security (see Instruction Sheet)	
<input checked="" type="checkbox"/> Back-up Person/Watch	<input type="checkbox"/> HP Coverage	<input type="checkbox"/> Posting/Warning Signs	<input type="checkbox"/> Time Limitation	<input type="checkbox"/> Other	
<input type="checkbox"/> Barricades	<input type="checkbox"/> IH Survey	<input type="checkbox"/> Scaffolding-requires inspection	<input type="checkbox"/> Warning Alarm (i.e. "high level")		
<b>Protective Equipment</b>					
<input type="checkbox"/> None	<input type="checkbox"/> Ear Plugs	<input type="checkbox"/> Gloves	<input type="checkbox"/> Lab Coat	<input checked="" type="checkbox"/> Safety Glasses	
<input type="checkbox"/> Coveralls	<input type="checkbox"/> Ear Muffs	<input type="checkbox"/> Goggles	<input type="checkbox"/> Respirator	<input checked="" type="checkbox"/> Safety Harness	
<input type="checkbox"/> Disposable Clothing	<input type="checkbox"/> Face Shield	<input checked="" type="checkbox"/> Hard Hat	<input type="checkbox"/> Shoe Covers	<input checked="" type="checkbox"/> Safety Shoes	<input type="checkbox"/> Other
<b>Permits Required (Permits must be valid when job is scheduled.)</b>					
<input checked="" type="checkbox"/> None	<input type="checkbox"/> Cutting/Welding	<input type="checkbox"/> Impair Fire Protection Systems			
<input type="checkbox"/> Concrete/Masonry Penetration	<input type="checkbox"/> Digging/Core Drilling	<input type="checkbox"/> Rad Work Permit-RWP No			
<input type="checkbox"/> Confined Space Entry	<input type="checkbox"/> Electrical Working Hot	<input type="checkbox"/> Other			
<b>Dosimetry/Monitoring</b>					
<input checked="" type="checkbox"/> None	<input type="checkbox"/> Heat Stress Monitor	<input type="checkbox"/> Real Time Monitor	<input type="checkbox"/> TLD		
<input type="checkbox"/> Air Effluent	<input type="checkbox"/> Noise Survey/Dosimeter	<input type="checkbox"/> Self-reading Pencil Dosimeter	<input type="checkbox"/> Waste Characterization		
<input type="checkbox"/> Ground Water	<input type="checkbox"/> O <sub>2</sub> /Combustible Gas	<input type="checkbox"/> Self-reading Digital Dosimeter	<input type="checkbox"/> Other Check O <sub>2</sub> level prior to entry		
<input type="checkbox"/> Liquid Effluent	<input type="checkbox"/> Passive Vapor Monitor	<input type="checkbox"/> Sorbent Tube/Filter Pump			
<b>Training Requirements (List below specific training requirements)</b>					
Confined Space, CA –Collider User, PHENIX Awareness					
<b>Based on analysis above, the Walkdown Team determines the risk, complexity, and coordination ratings below:</b>			<b>If using the permit when all hazard ratings are low, only the following need to sign: ( Although allowed, there is no need to use back of form)</b>		
<b>ES&amp;H Risk Level:</b>	<input checked="" type="checkbox"/> Low	<input type="checkbox"/> Moderate	<input type="checkbox"/> High	WCC:	Date:
<b>Complexity Level:</b>	<input checked="" type="checkbox"/> Low	<input type="checkbox"/> Moderate	<input type="checkbox"/> High	Service Provider:	Date:
<b>Work Coordination:</b>	<input checked="" type="checkbox"/> Low	<input type="checkbox"/> Moderate	<input type="checkbox"/> High	Authorization to start	Date:
(Departmental Sup/WCC/Designee)					

3. Both work requester and service provider contribute to work plan (use attachments for detailed plans)

<b>Work Plan</b> (procedures, timing, equipment, and personnel availability need to be addressed): See Attached Work Plan				
Special Working Conditions Required: None				
Operational Limits Imposed: Modification work limited to lower octants easily reachable when standing on lower magnet superstructure.				
Post Work Testing Required: No				
Job Safety Analysis Required: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No			Walkdown Required: <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
<b>Reviewed by:</b> Primary Reviewer will determine the size of the review team and the other signatures required based on hazards and job complexity. Primary Reviewer signature means that the hazards and risks that could impact ES&H have been identified and will be controlled according to BNL requirements.				
<b>Title</b>	<b>Name (print)</b>	<b>Signature</b>	<b>Life #</b>	<b>Date</b>
Primary Reviewer				
ES&H Professional				
Other				
Other				
Work Control Coordinator				
Service Provider				
Review Done: <input type="checkbox"/> in series		<input type="checkbox"/> team		

**4. Job site personnel fill out this section.**

Note: Signature indicates personnel performing work have read and understand the hazards and permit requirements (including any attachments).			
Job Supervisor:		Contractor Supervisor:	
Workers:	Life#:	Workers :	Life#:
Workers are encouraged to provide feedback on ES&H concerns or on ideas for improved job work flow. Use feedback form or space below.			

**5. Departmental Job Supervisor, Work Control Coordinator/Designee**

Conditions are appropriate to start work: (Permit has been reviewed, work controls are in place and site is ready for job.)			
Name:	Signature:	Life#:	Date:

**6. Departmental Job Supervisor, Work Requester/Designee determines if Post Job Review is required.** ☐ Yes ☐ No

Post Job Review (Fill in names of reviewers)			
Name:	Signature:	Life#:	Date:
Name:	Signature:	Life#:	Date:

**7. Worker provides feedback.**

Worker Feedback (use attached sheets as necessary)	
a) WCM/WCC: Is any feedback required? <input type="checkbox"/> Yes <input type="checkbox"/> No	
b) Workers: Are there better methods or safer ways to perform this job in the future? <input type="checkbox"/> Yes <input type="checkbox"/> No	

**8. Closeout: Work Control Coordinator (authorizing dept.) checks quality of completed permit and ensures the work site is left in an acceptable condition. (WCC can delegate clean up of work area to work supervisor)**

Name:	Signature:	Life#:	Date:
Comments:			

## **RPC2 Prototype Installation**

### **Introduction**

As a part of the PHENIX Muon Trigger Upgrade, 2 prototype detectors are to be installed in the PHENIX experiment complex. The first prototype (RPC2) will be installed on the north side of the south MuID detector in the PHENIX IR. The other prototype (RPC3) will be installed in the RHIC tunnel (sector 7) on the south side of the south MuID detector. This procedure is for the RPC2 prototype only, RPC3 will be installed by CAD personnel in accordance with a separate and distinct work plan.

The purpose of the prototype test is to assess the ability of the RPC design in the PHENIX experiment ambient conditions as well as to test the electronics, and the customized detector gas environment in the rigors of an experimental run.

### **Work Plan**

This work is to be done by fully trained and experienced personnel (PHENIX mechanical and electrical technicians and RPC expert scientists) during the 2008 summer shutdown. All persons participating in the installation shall have current PHENIX Awareness and CA access. In addition, technicians participating in the installation shall have appropriate crane training, working at height training, manlift operation and/or electrical safety training as appropriate for the tasks being performed.

#### **1. Preparation for installation**

- RPC experts shall assemble and test the prototype in the RPC factory and have the prototype ready for installation when required by PHENIX technicians.
- Survey and prepare mounting points to suspend the RPC2 from (see figure 1).
- Load test suspension fixtures (wire rope, terminators) to certify the equipment for this application. And mount the fixtures with the wire rope hanging in their approximate final resting position.
- Prepare slings to orient RPC2 during installation. (See figure 2 for center of gravity info).


#### **2. Prototype Transportation**


- PHENIX techs shall arrange with BNL trades to have the prototype transported from the RPC factory to the PHENIX Assembly Hall (AH). Care shall be taken to assure that the

prototype is not jostled or otherwise mishandled during transport.

### **3. Installation**

- Carefully lift the RPC2 in the AH using the slings prepared in step 1.
- Move RPC2 around the East Carriage (EC) in the AH using the AH crane and set the RPC2 down on the 12 ton cart for transport into the Interaction Region (IR).
- Once in the IR re-rig the RPC2 with the IR crane and slowly lift and move the prototype to its installed position.
- Attach the suspension wires to the swivel hooks provided and slowly transfer the load from the crane/slugs to the suspension wires.
- Disconnect the slugs and move the slugs/crane away from the RPC2.
- Adjust the wires using the provided turnbuckles to level and position the RPC2 prototype as close as possible to its nominal installed position. Use the lower adjustment rods to remove any roll and yaw.
- After the RPC2 is installed, survey the 10 marked bolt heads and provide the survey info to RPC experts.
- Document all issues and problems encountered on the work permit.

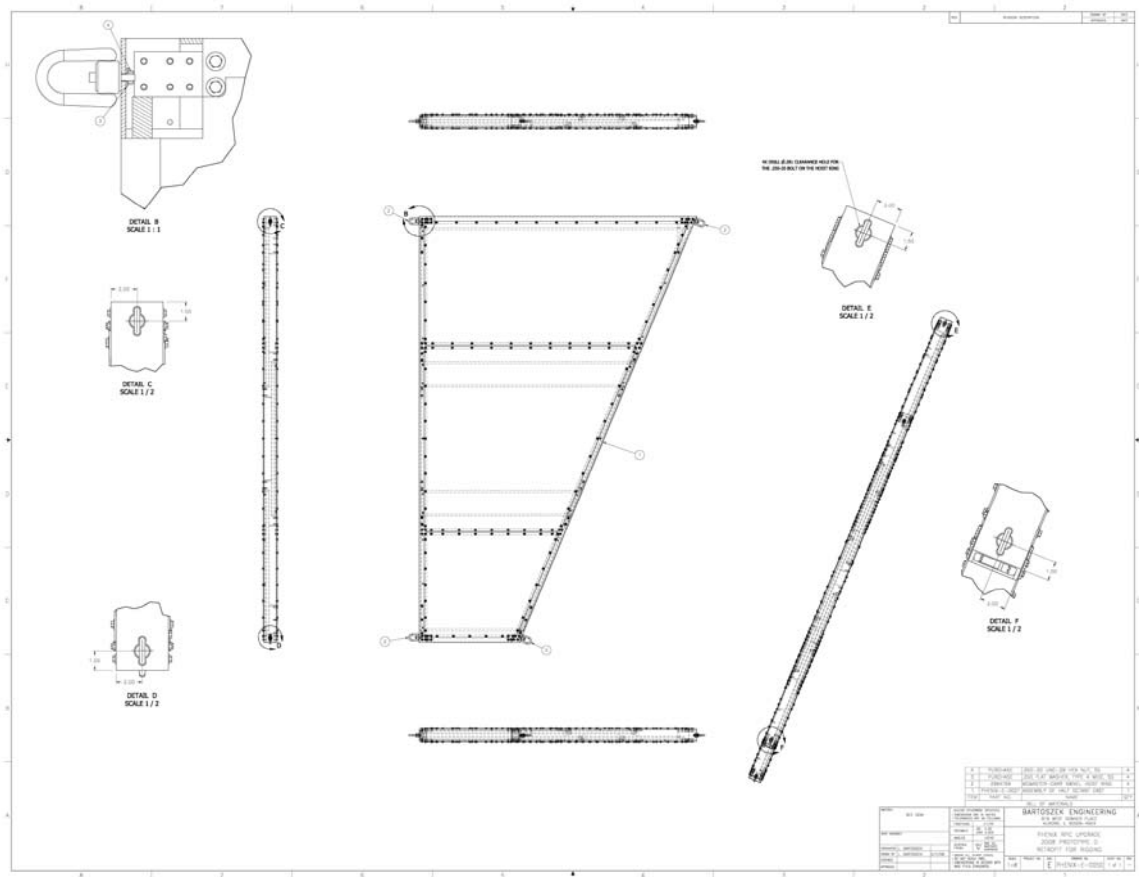

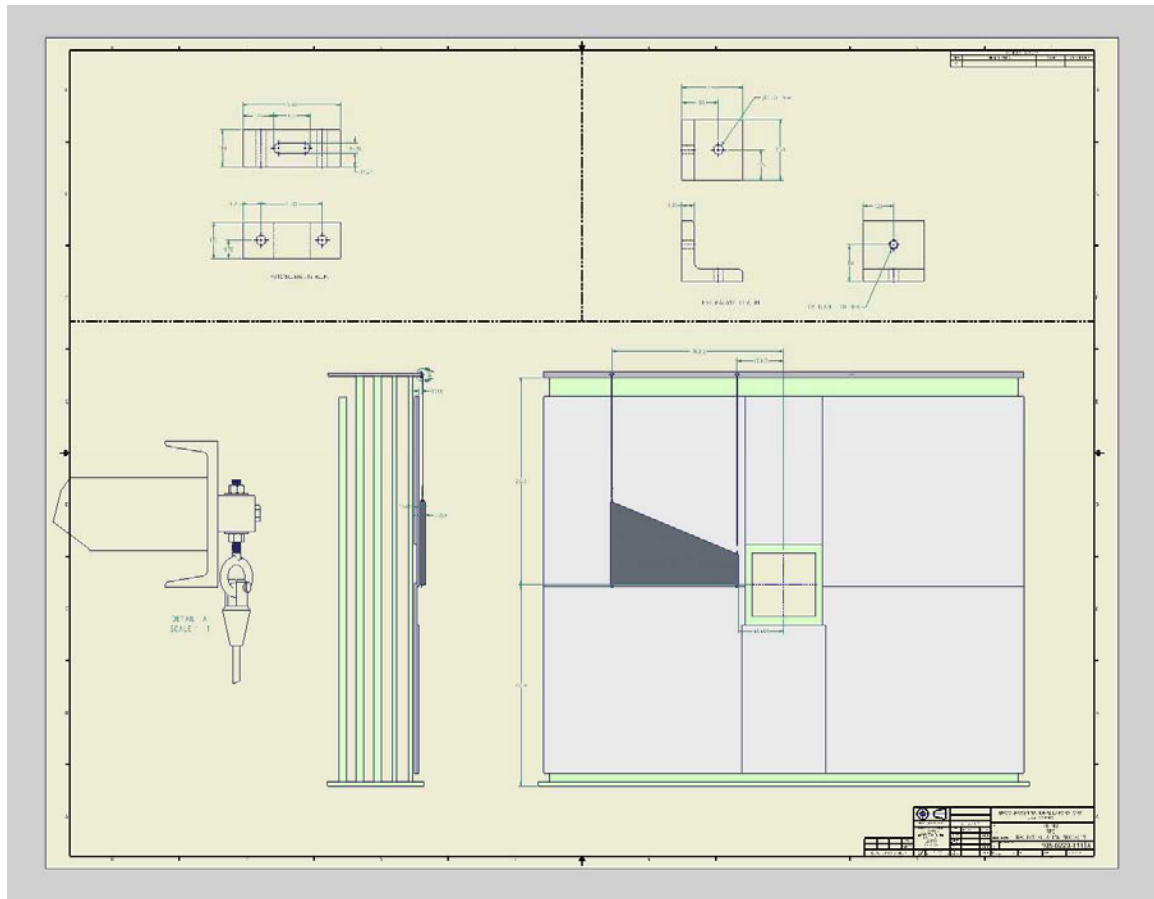

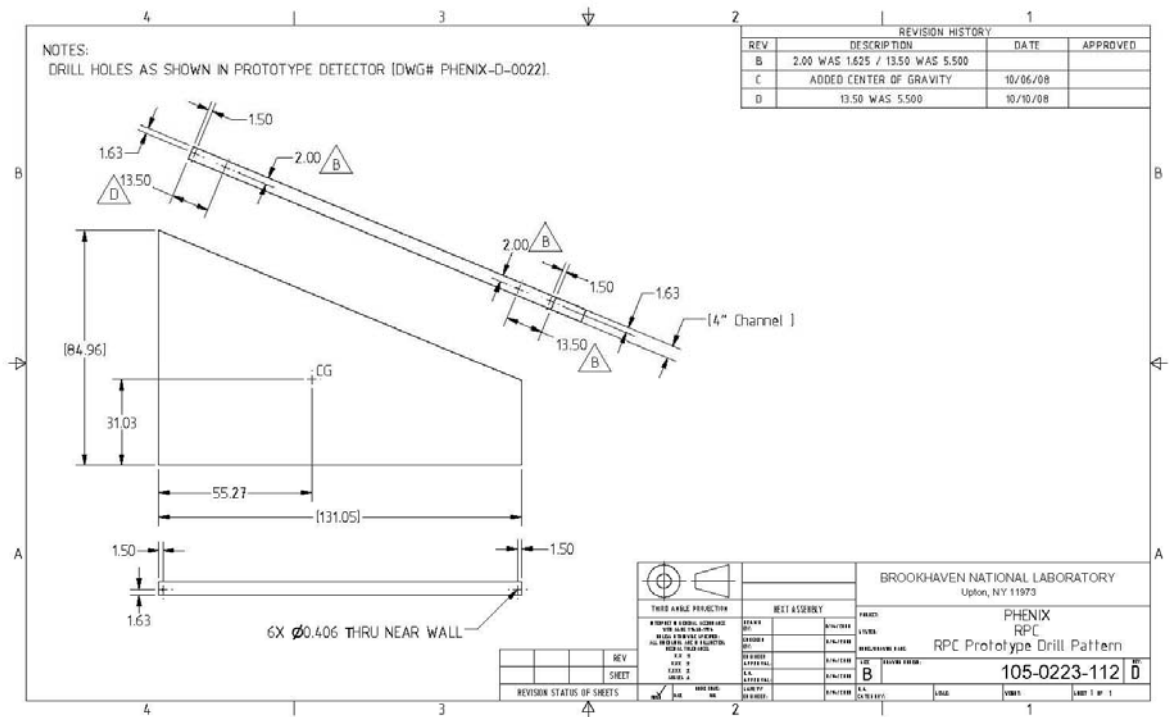


Figure 2: Prototype RPC2 Center of Gravity  
(PHENIX Drawing #105-0223-112D)
